




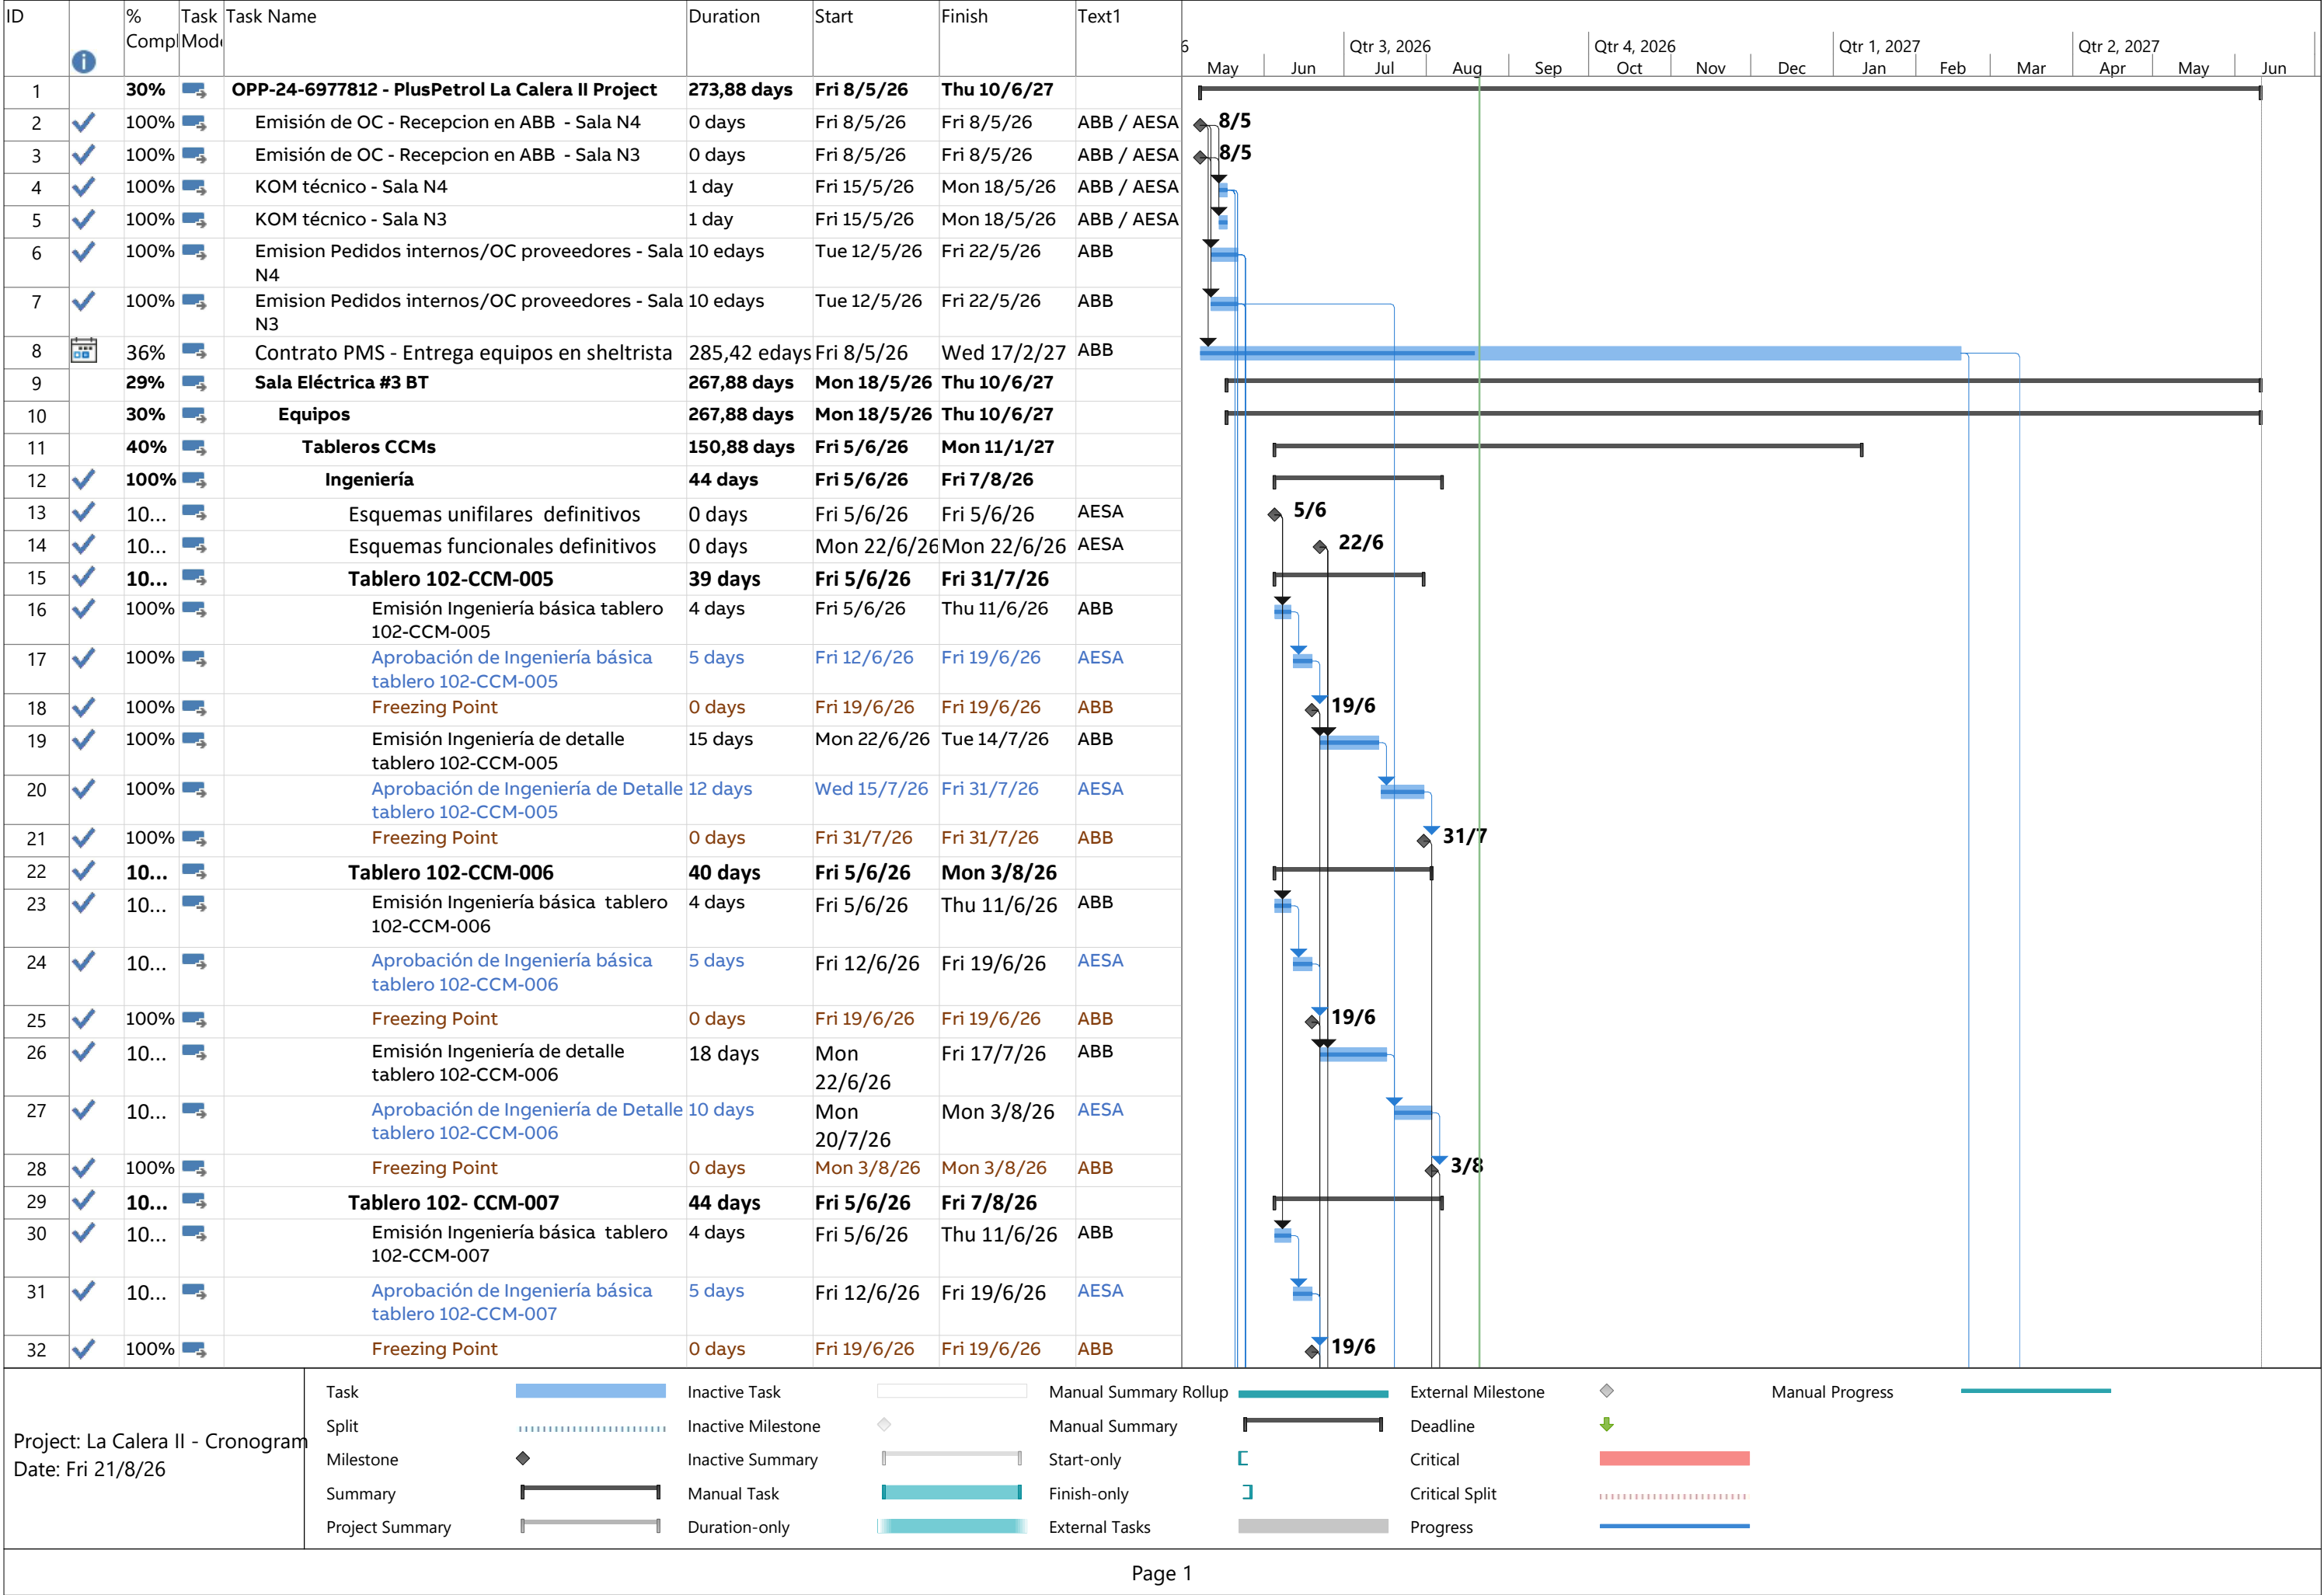

Project: La Calera II - Cronogram
Date: Fri 21/8/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress


Manual Progress

Page 2


ID		% Comp	Task Mod	Task Name	Duration	Start	Finish	Text1	6 MayJunQtr 3, 2026JulAugSepQtr 4, 2026OctNovDecQtr 1, 2027JanFebMarQtr 2, 2027AprMayJun															
66		13%		Drives BT	160,88 days	Fri 22/5/26	Tue 12/1/27																	
67		10...		Emisión ingeniería básica	37 days	Fri 22/5/26	Thu 16/7/26	ABB																
68		10...		Aprobación de ingeniería - Confirmación de slot de fabricación	10 days	Thu 16/7/26	Thu 30/7/26	AESA																
69		10...		Freezing Point	0 days	Thu 30/7/26	Thu 30/7/26	ABB																
70		50%		Emisión ingeniería de detalle	31 days	Thu 30/7/26	Fri 11/9/26	ABB																
71		0%		Aprobación de ingeniería de detalle	10 days	Fri 11/9/26	Fri 25/9/26	AESA																
72		0%		Freezing Point	0 days	Fri 25/9/26	Fri 25/9/26	ABB																
73		0%		Acopio y fabricación	60 edays	Fri 21/8/26	Tue 20/10/26	ABB																
74		0%		Despacho fábrica de origen	5 days	Tue 20/10/26	Tue 27/10/26	ABB																
75		0%		Traslado internacional + aduana	75 edays	Tue 27/10/26	Sun 10/1/27	ABB																
76		0%		Entrega en Shelterista	2 days	Mon 11/1/27	Tue 12/1/27	ABB																
77		49%		Rectificadores/UPS/Baterias	136 days	Mon 18/5/26	Thu 26/11/26																	
78		10...		Datos técnicos confirmados en etapa de licitación	0 days	Mon 18/5/26	Mon 18/5/26	AESA																
79		100%		Emisión de ingeniería básica	25 days	Mon 18/5/26	Tue 23/6/26	ABB																
80		100%		Aprobación de ingeniería básica con comentarios	8 days	Tue 23/6/26	Fri 3/7/26	AESA																
81		100%		Freezing Point	0 days	Fri 3/7/26	Fri 3/7/26	ABB																
82		48%		Compra y Acopio de Materiales	88 days	Tue 9/6/26	Mon 12/10/26	ABB																
83		60%		Baterias	85 days	Tue 9/6/26	Wed 7/10/26	ABB																
84		45%		Gabinetes y accesorios	65 days	Mon 13/7/26	Mon 12/10/26	ABB																
85		45%		Magnéticos y Semiconductores	60 days	Mon 13/7/26	Mon 5/10/26	ABB																
86		45%		Interruptores y Fusibles	60 days	Mon 13/7/26	Mon 5/10/26	ABB																
87		40%		Disipadores y capacitores	55 days	Mon 20/7/26	Mon 5/10/26	ABB																
88		0%		Fabricación	7 days	Mon 12/10/26	Wed 21/10/26	ABB																
89		0%		Ensayos internos	7 days	Thu 22/10/26	Mon 2/11/26	ABB																
90		0%		Ensayos - FAT	2 days	Mon 9/11/26	Wed 11/11/26	ABB / AESA																
91		0%		Acondicionamiento y embalaje	3 days	Wed 11/11/26	Mon 16/11/26	ABB																
92		0%		Condicion EXW	5 days	Mon 16/11/26	Mon 23/11/26	ABB																
93		0%		Entrega en Shelterista	3 days	Mon 23/11/26	Thu 26/11/26	ABB																
94		36%		Tableros Auxiliares	147 days	Fri 22/5/26	Fri 18/12/26																	
95		100%		Emisión ingeniería básica	35 days	Fri 22/5/26	Tue 14/7/26	ABB																
96		100%		Aprobación de Ingeniería Básica	6 days	Tue 14/7/26	Wed 22/7/26	AESA																
97		100%		Freezing Point	0 days	Wed 22/7/26	Wed 22/7/26	ABB																
98		100%		Emisión Ingeniería de detalle	16 days	Wed 22/7/26	Thu 13/8/26	ABB																
99		50%		Aprobación de Ingeniería de Detalle	10 days	Thu 13/8/26	Thu 27/8/26	AESA																
100		0%		Freezing Point	0 days	Thu 27/8/26	Thu 27/8/26	ABB																
101		27%		Acopio de Materiales	110 edays	Wed 22/7/26	Mon 9/11/26	ABB																
102		0%		Fabricación	20 days	Mon 9/11/26	Mon 7/12/26	ABB																

Project: La Calera II - Cronogram
Date: Fri 21/8/26

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

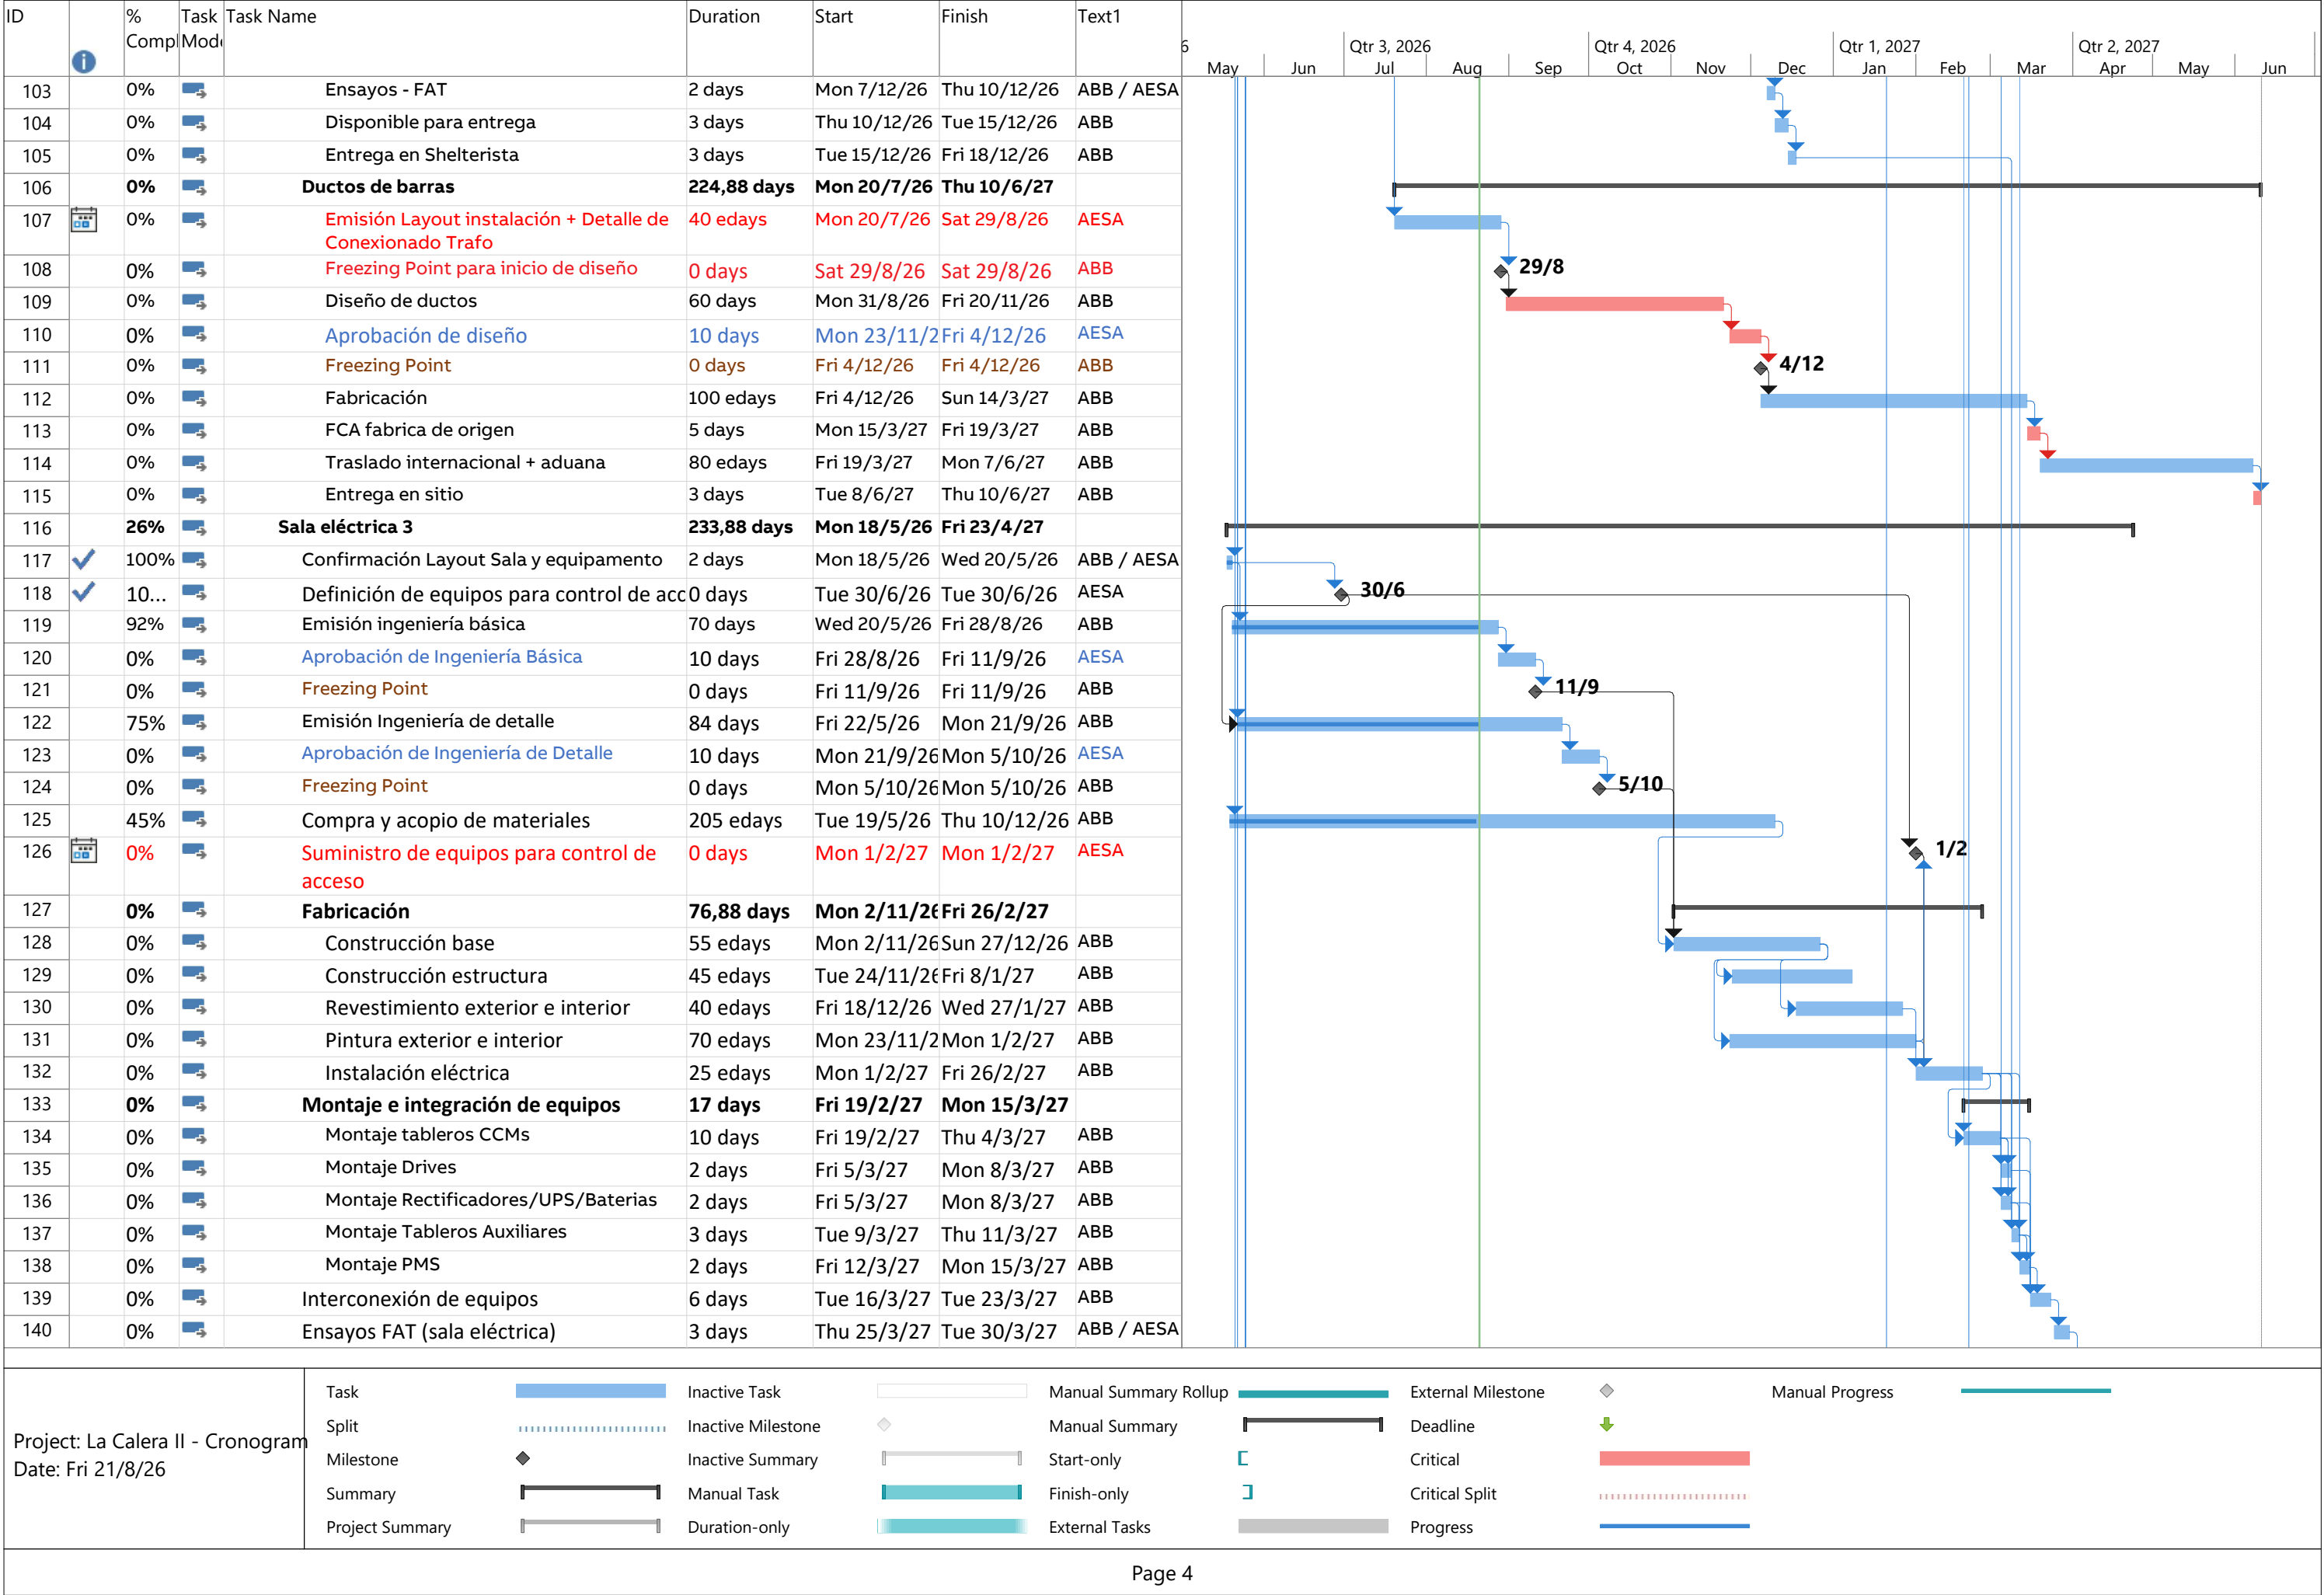

Page 4

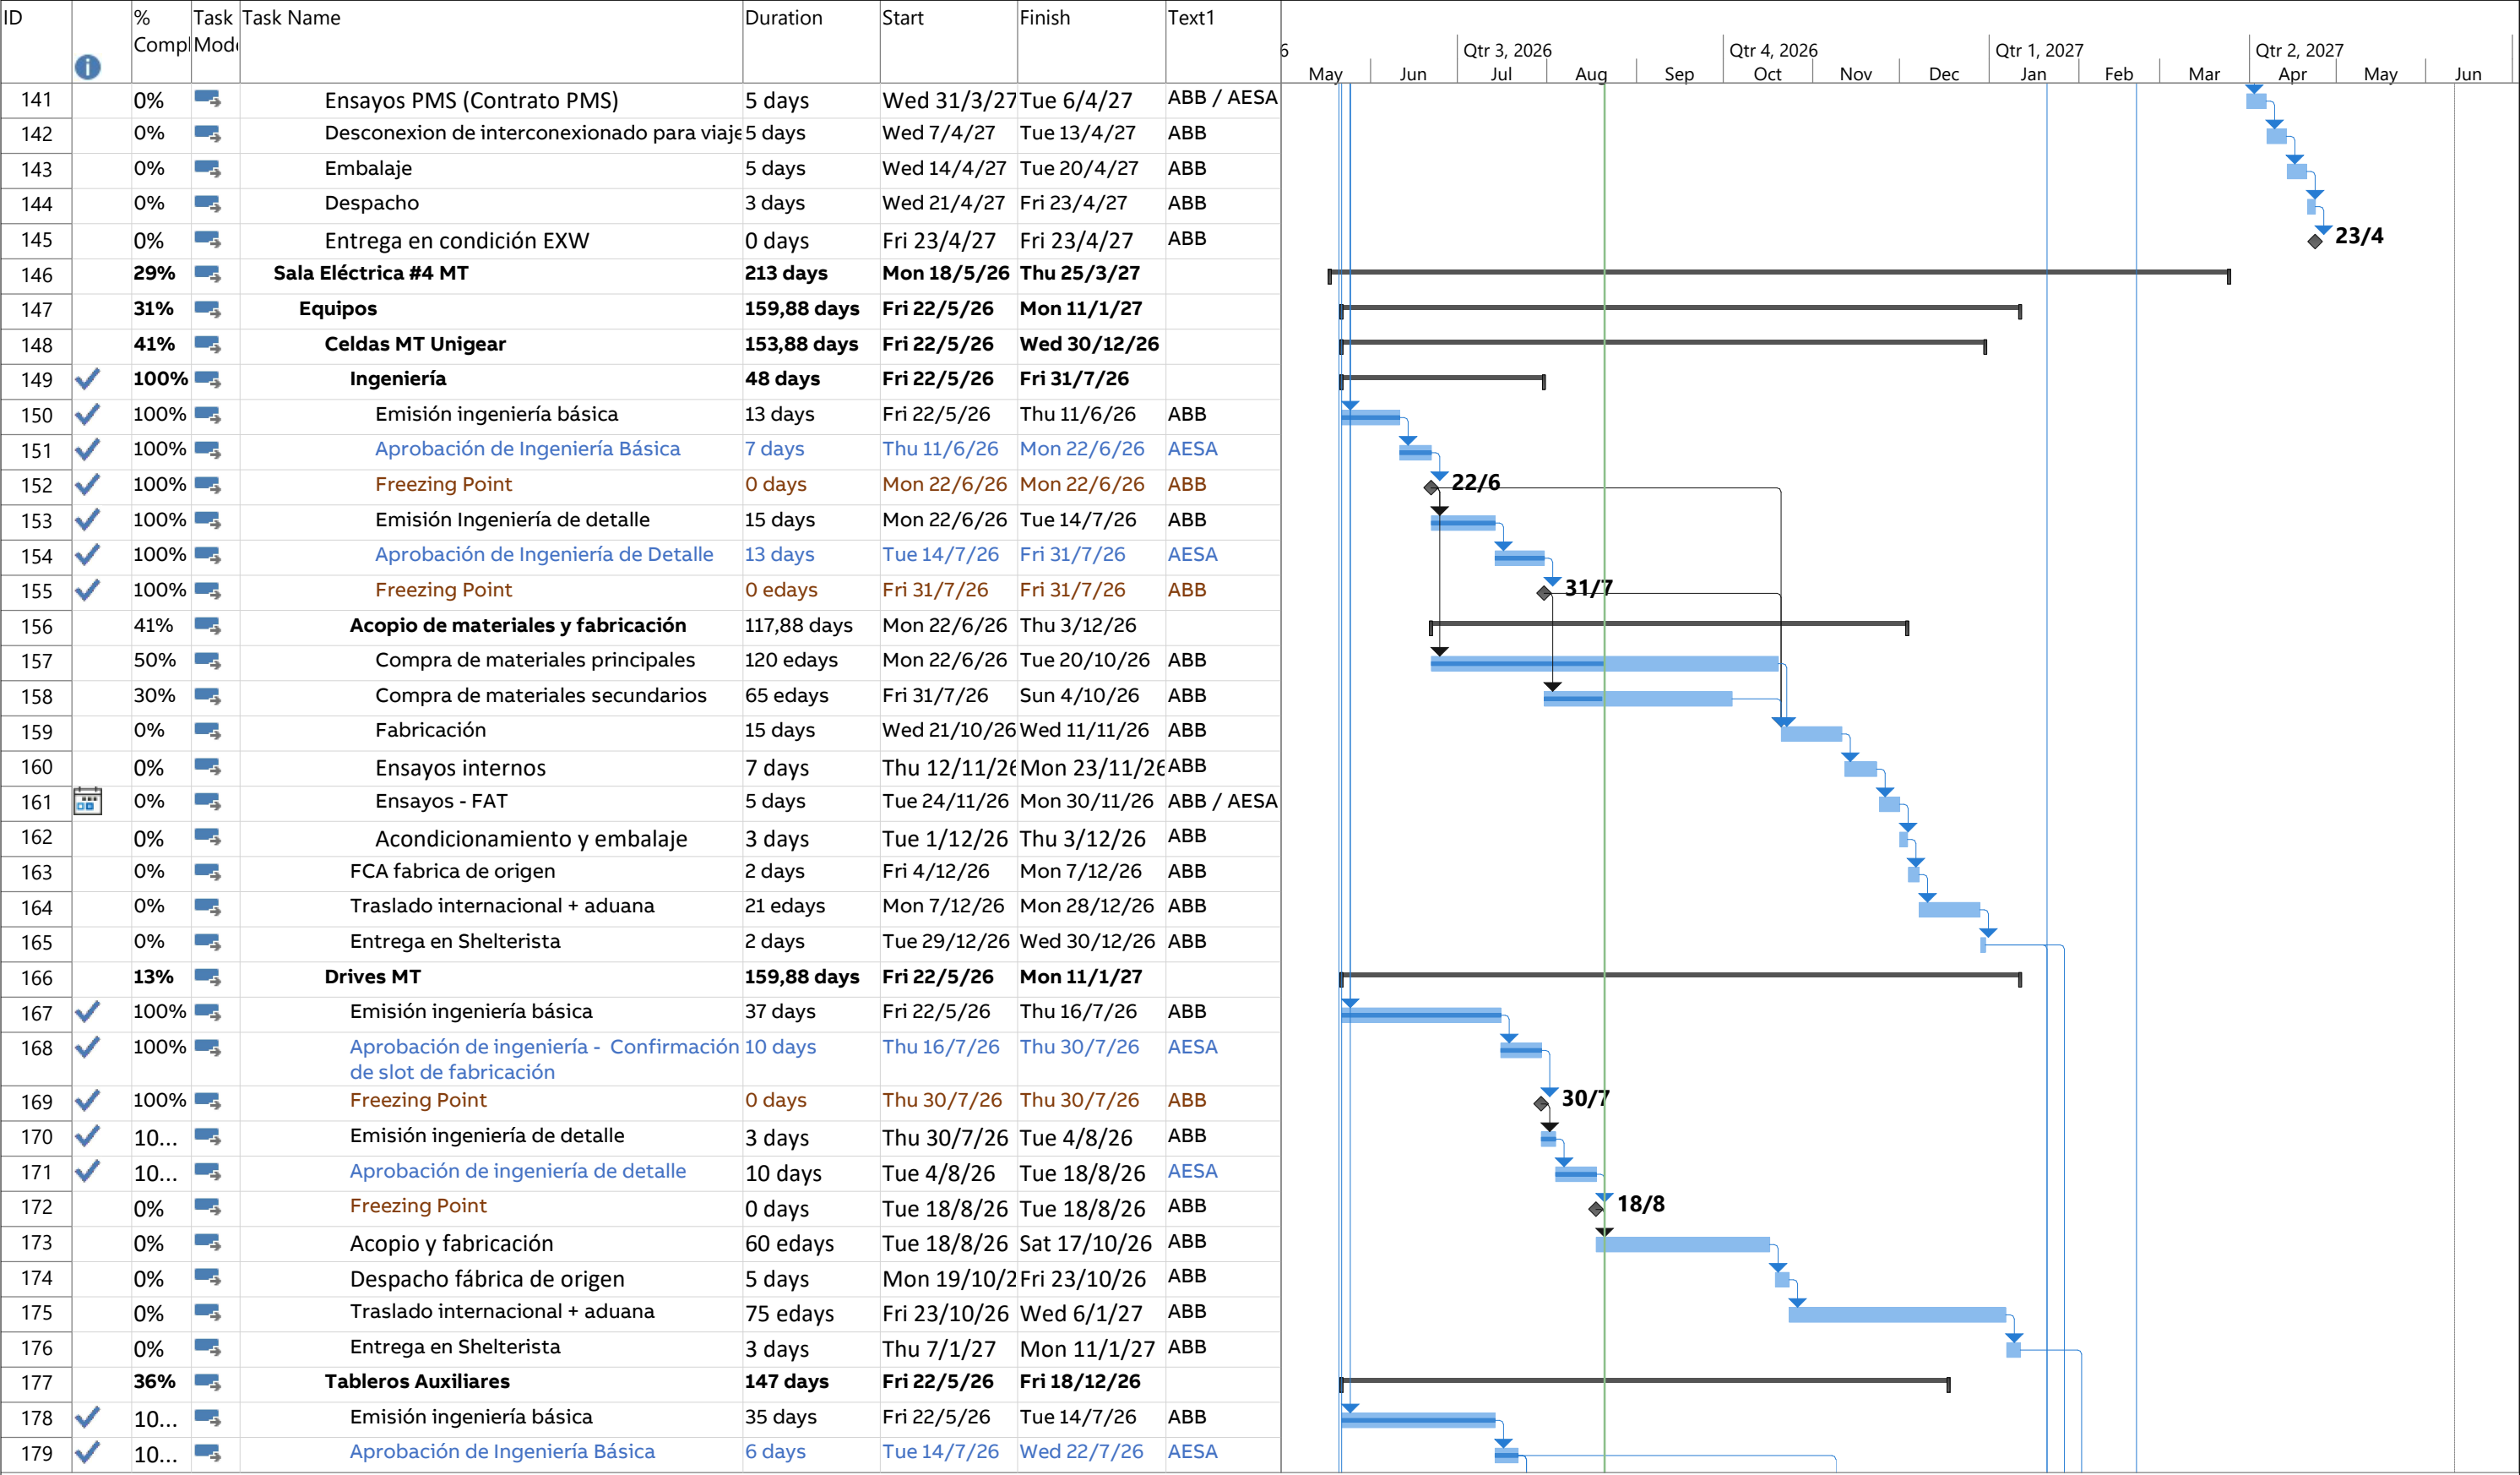

Project: La Calera II - Cronogram

Date: Fri 21/8/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline


Critical

Critical Split

Progress

Manual Progress

Page 5

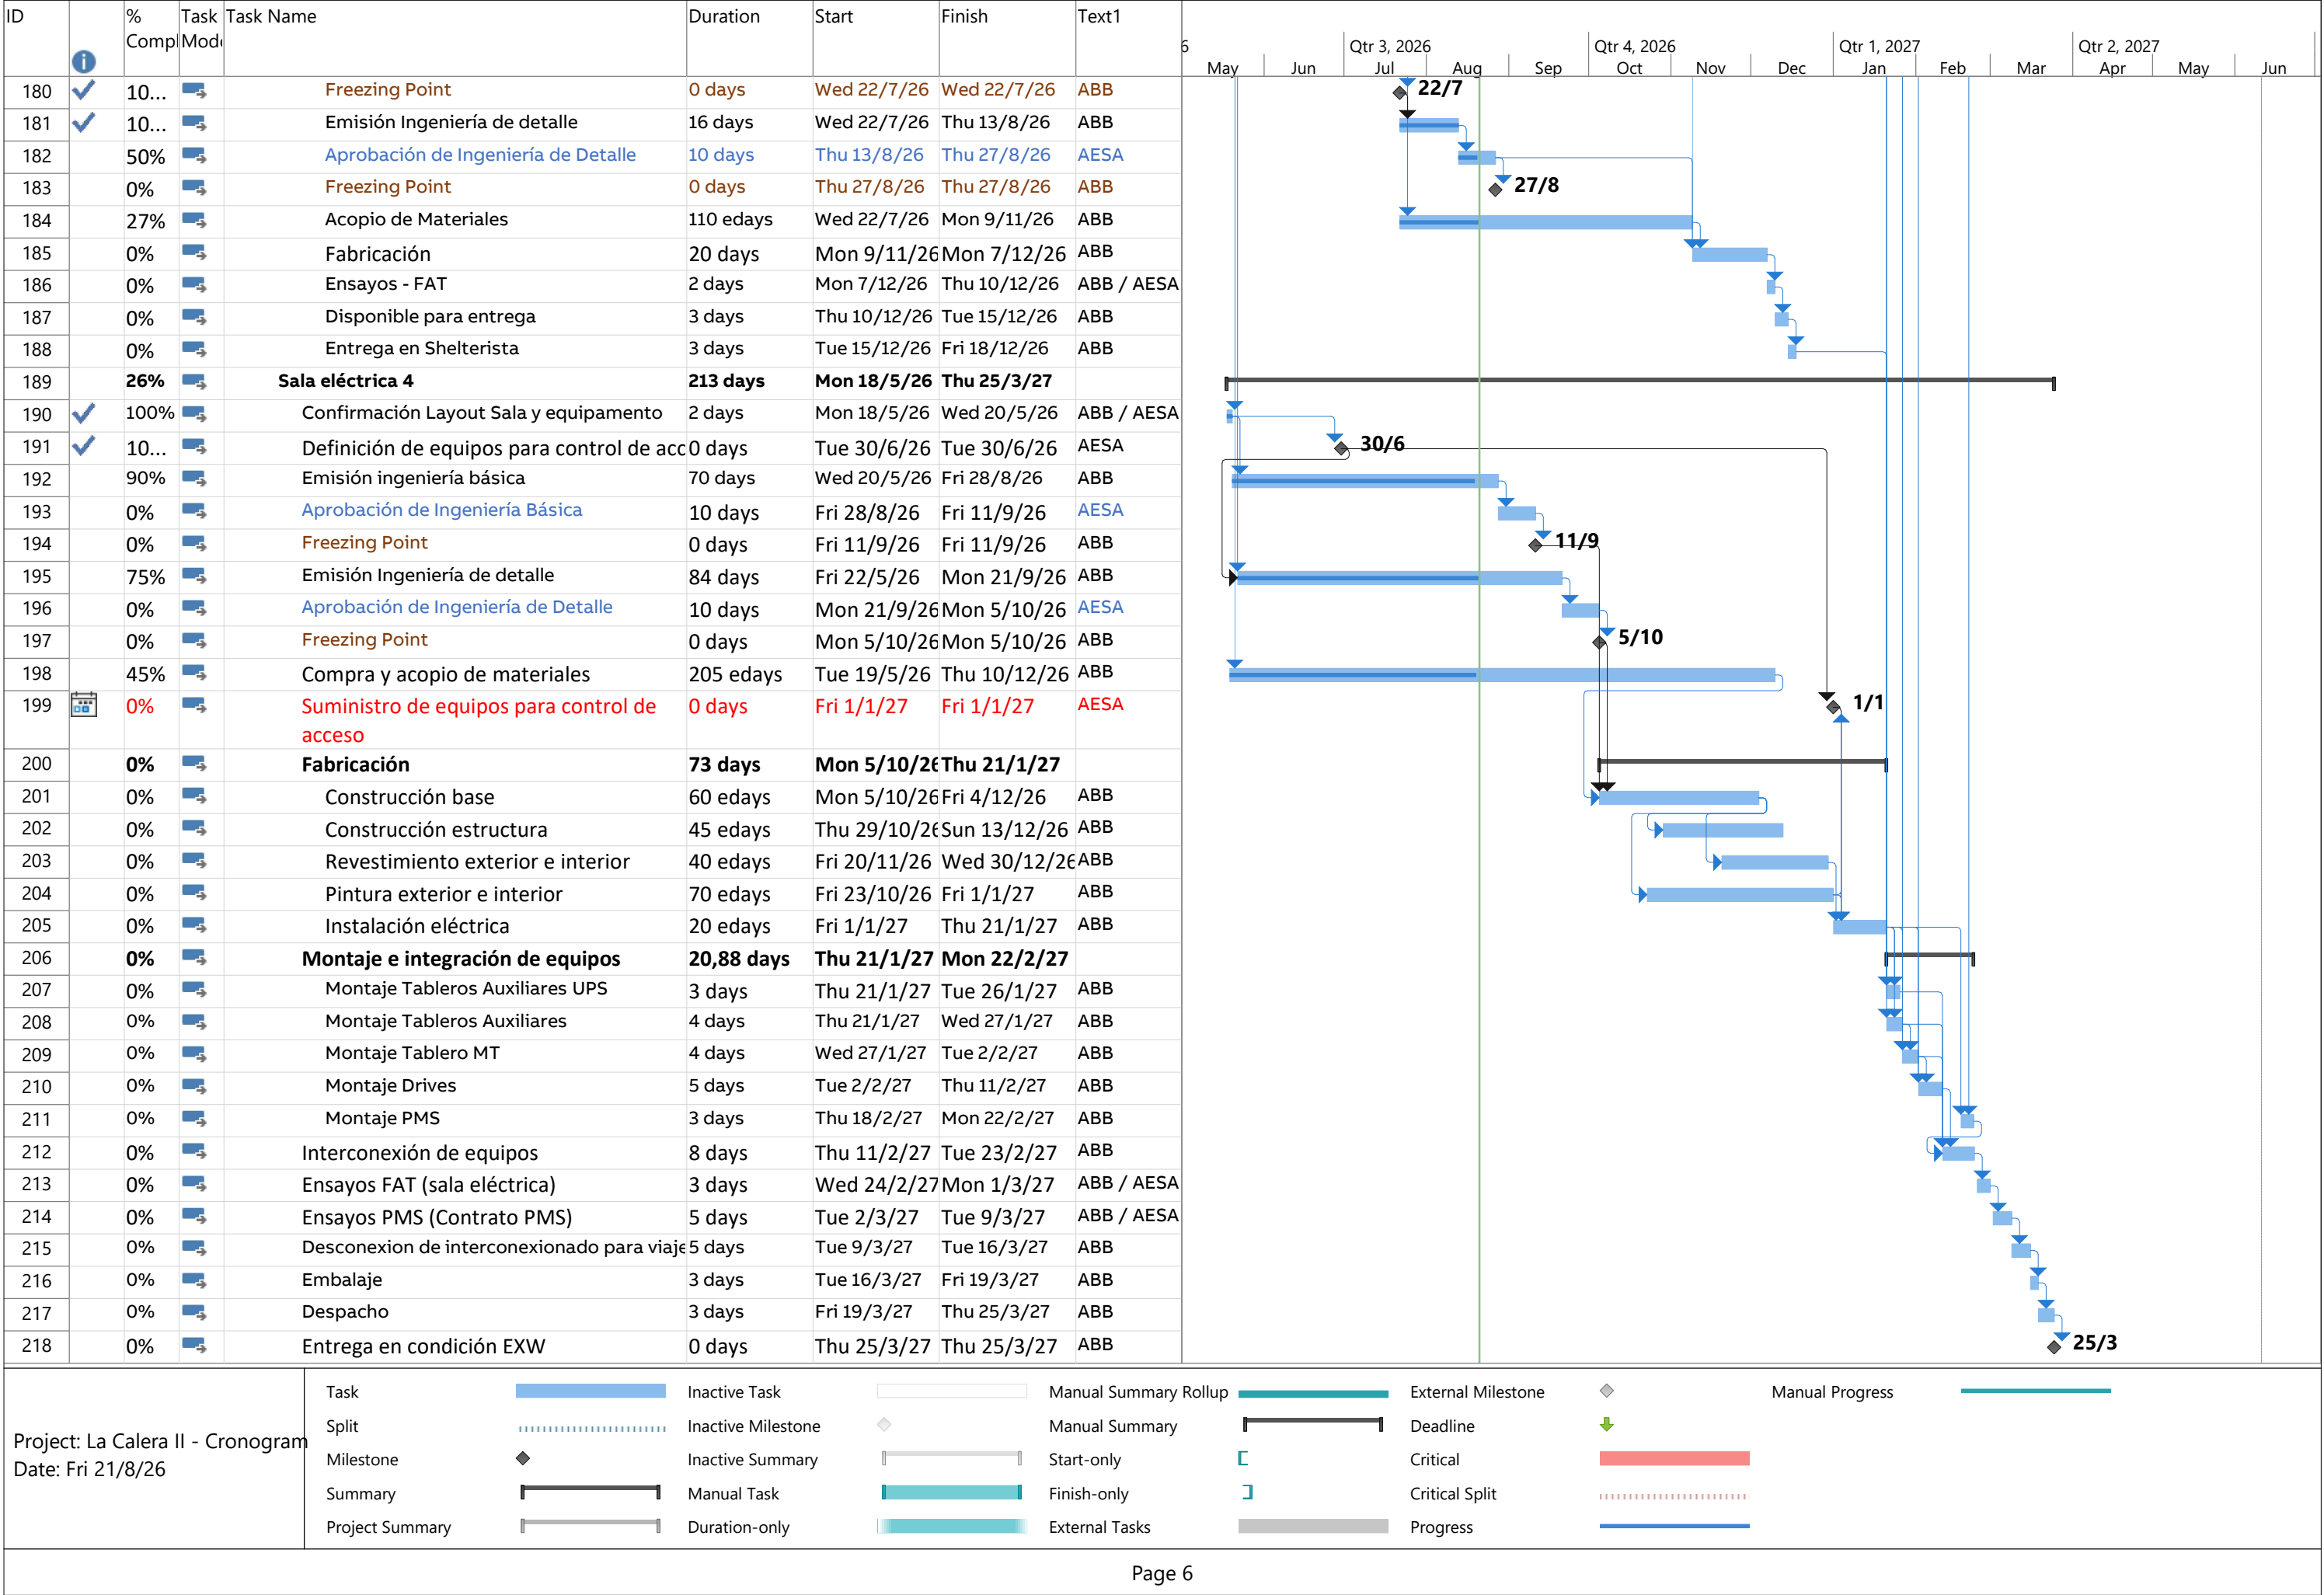

Page 6
