



A	PARA APROBACIÓN	4/6/2026	RM	RM	RM
REV.	DESCRIPTION	DATE	BY	CHK.	APPD


	AESA N° <u>5155-00-0009-VE-CO-PG-001</u> PROVEEDOR N° _____
---	--


 pluspetrol	JOB: PRODUCTION FACILITIES – LA CALERA	
	TITLE: CRONOGRAMA	
FACILITIES ENGINEERING & MAJOR PROJECTS	DOCUMENT N°: P00001-D-AESA-ACAL-00102-AABX-SELC-PP-X-0001	REVISION: A
All the information contained in this document is confidential and property of Pluspetrol, and the totally or partial copy or reproduction of it is prohibited without previous authorization.	SCALE: -	Page: 1 of 7
	REPLACE:	

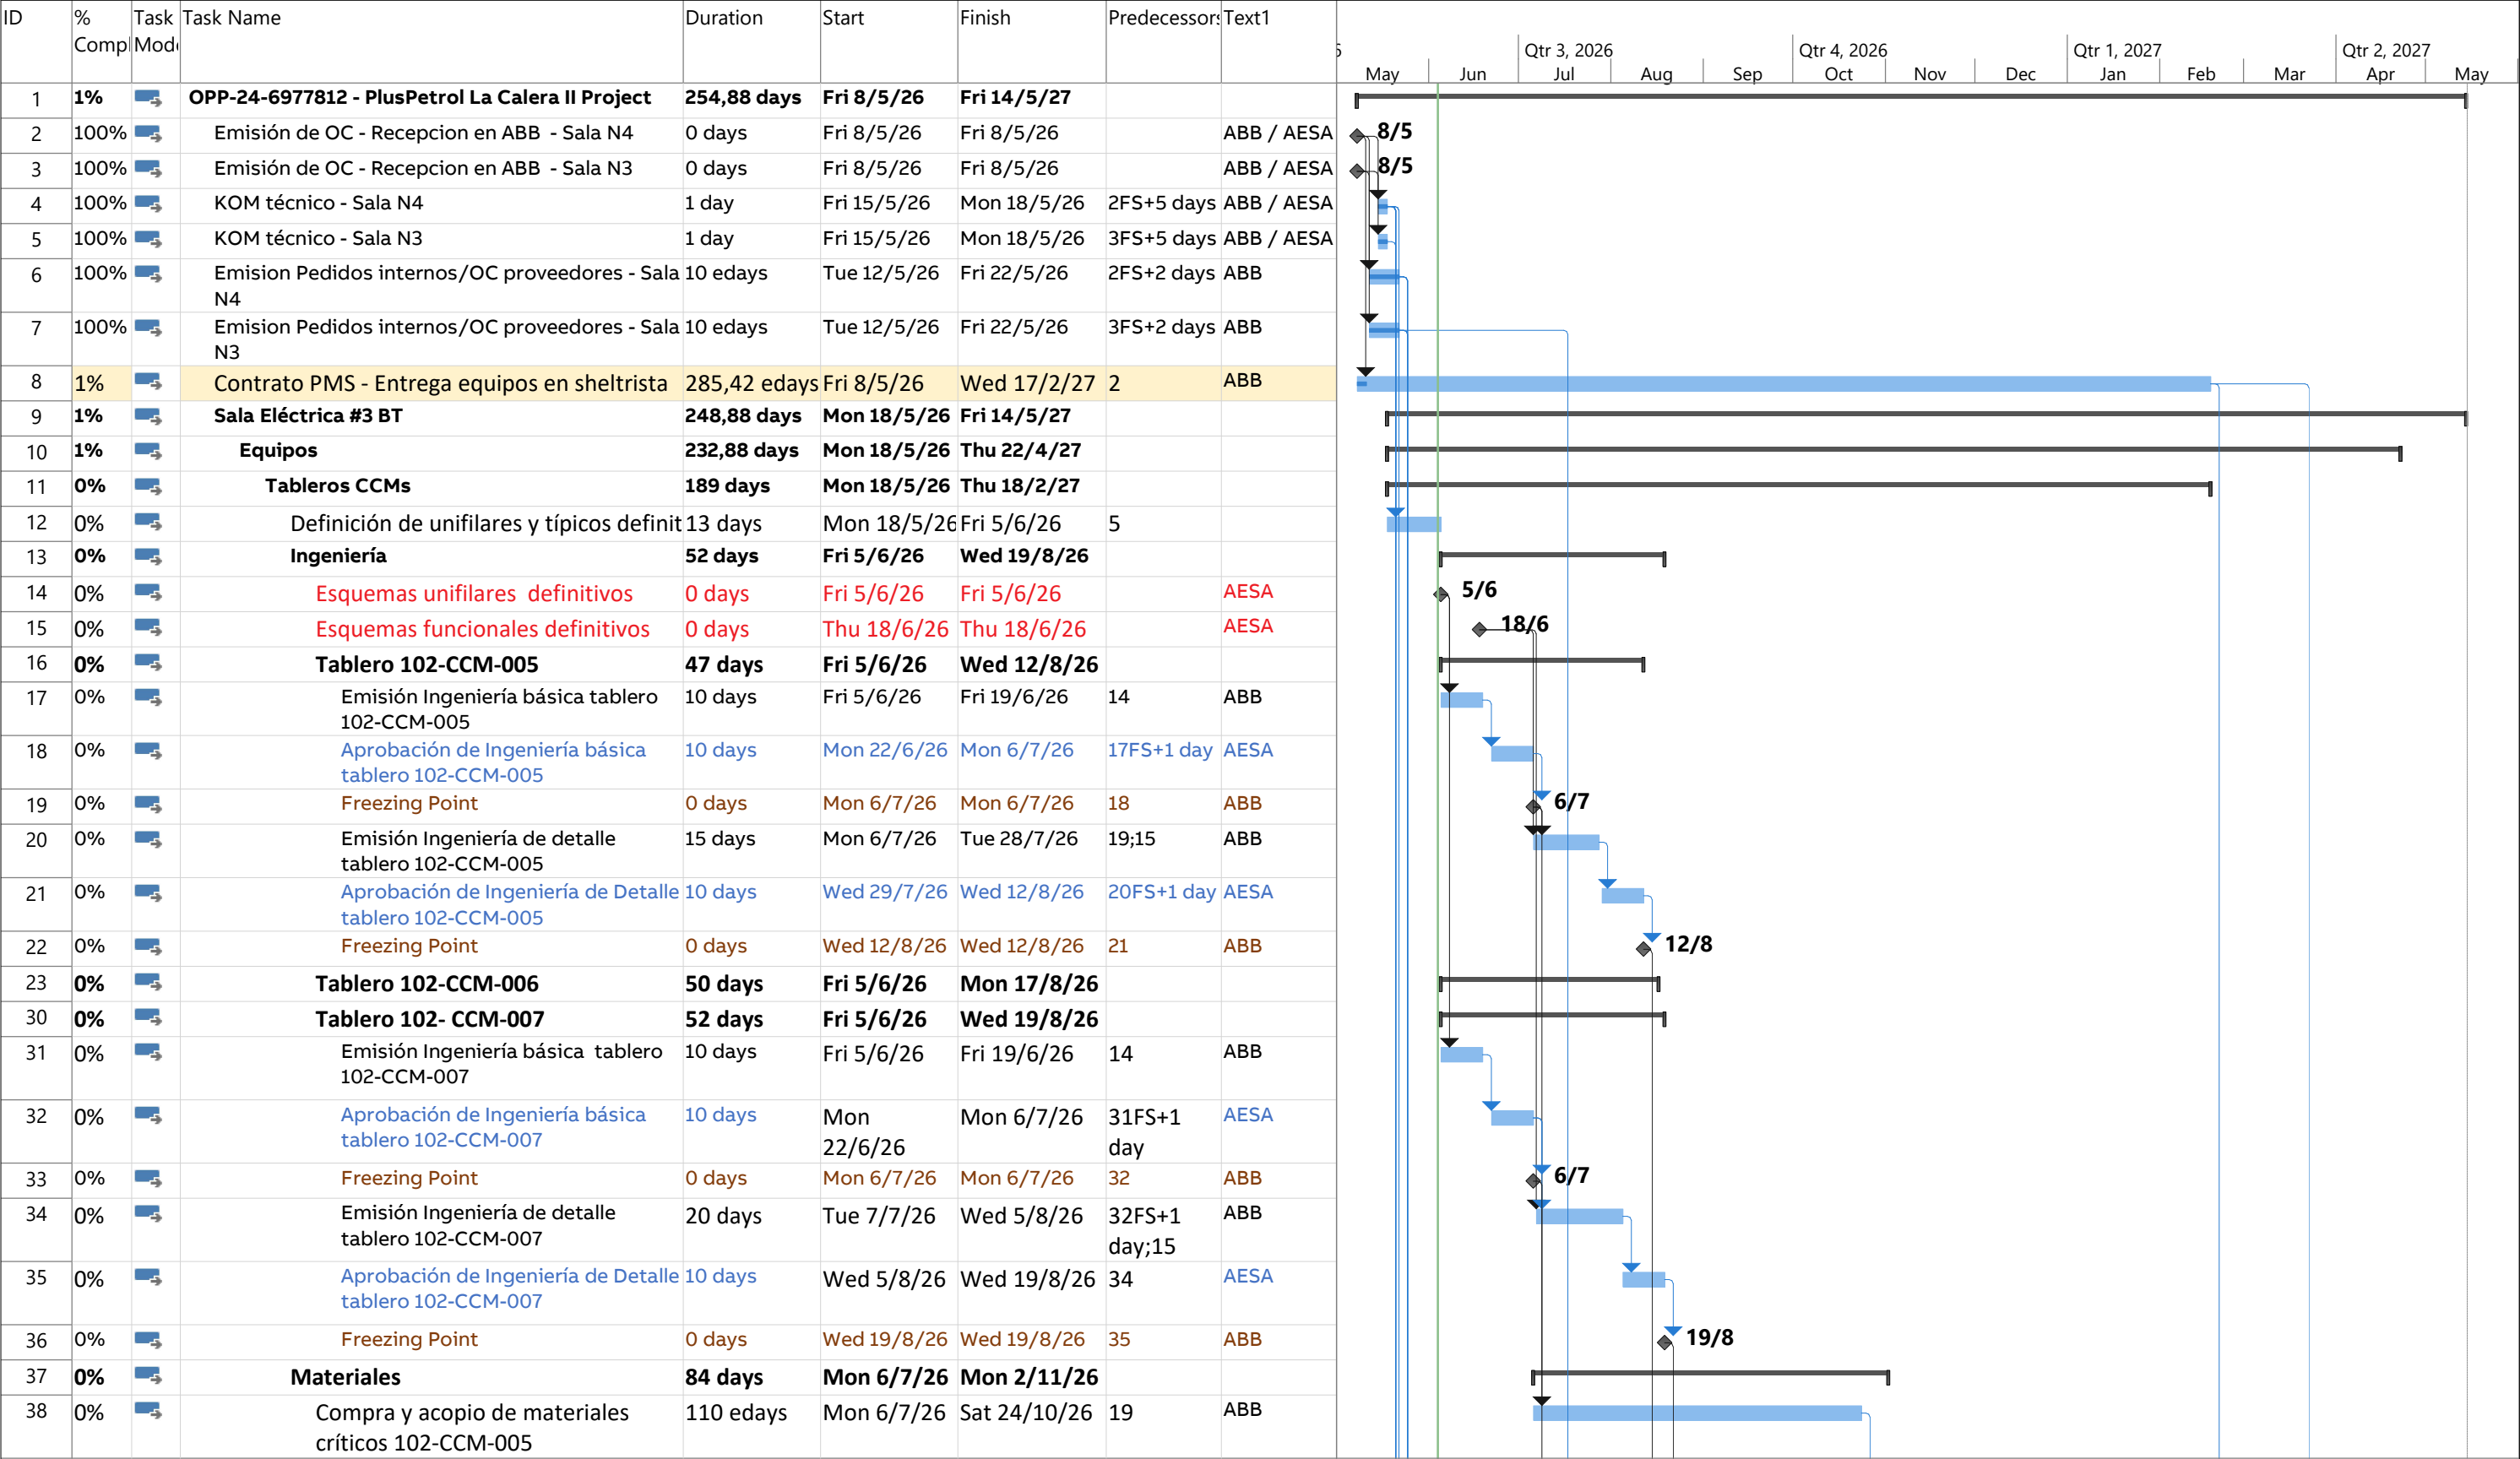


Page 1

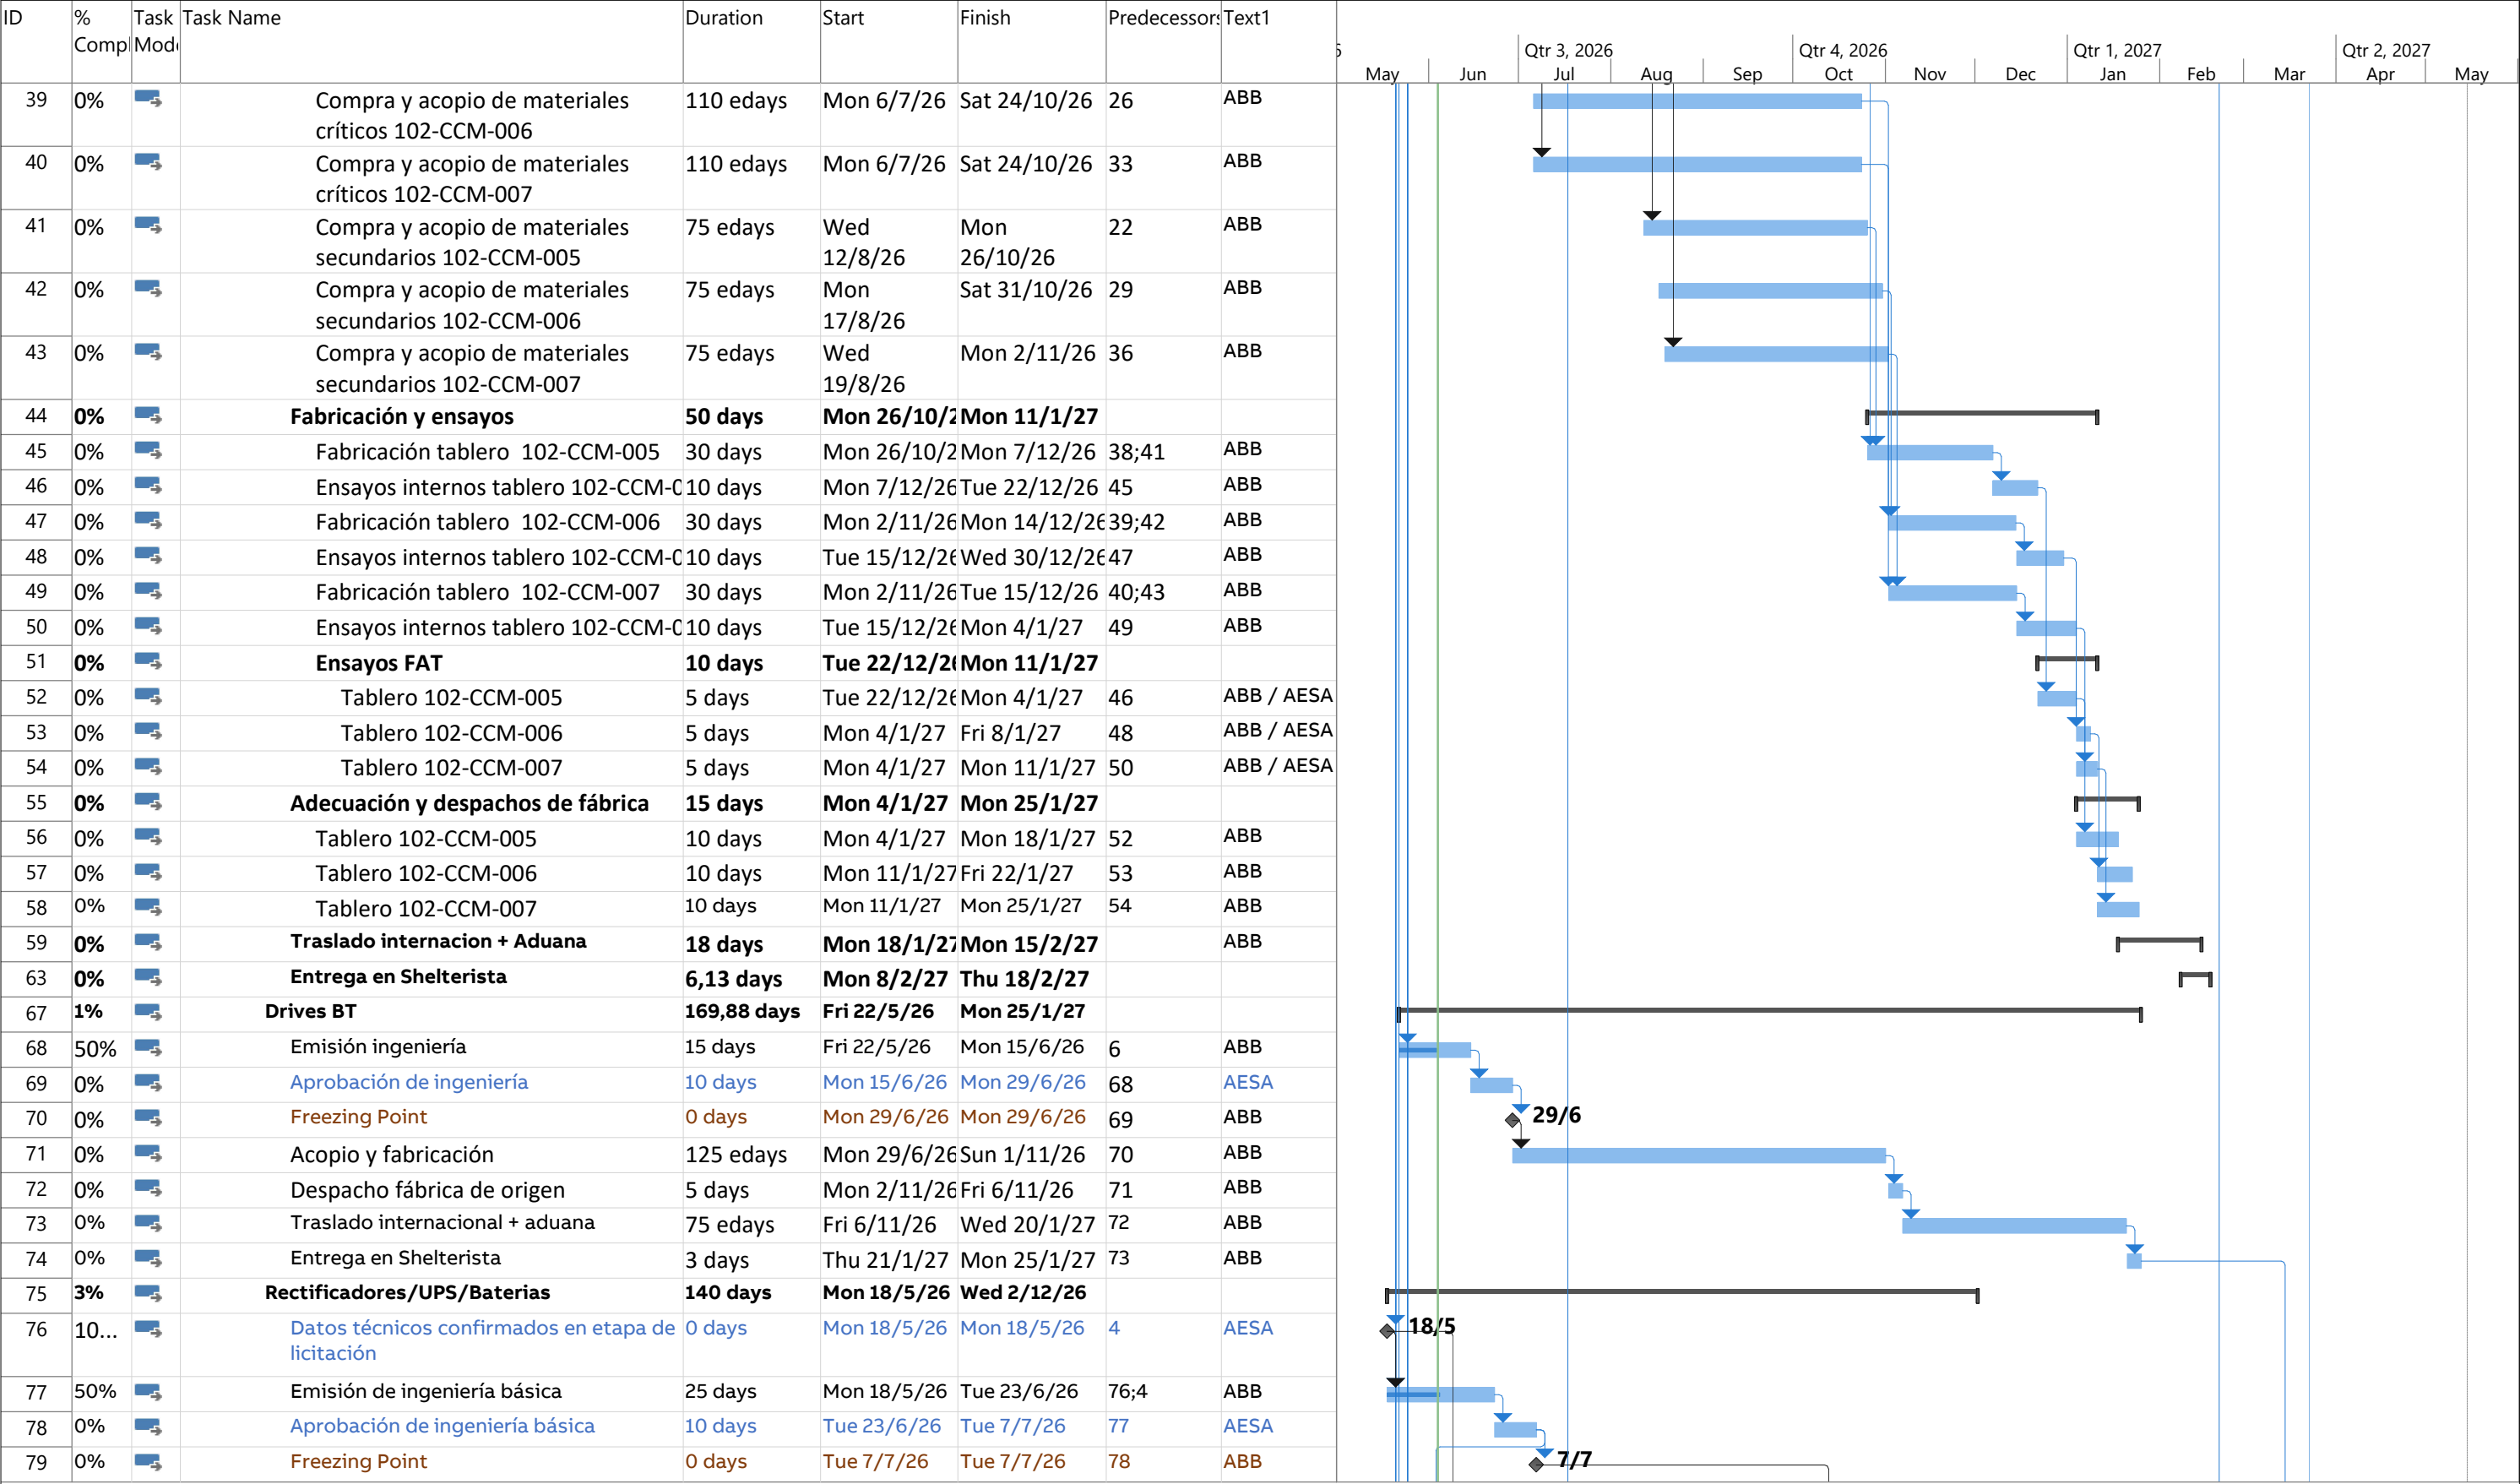

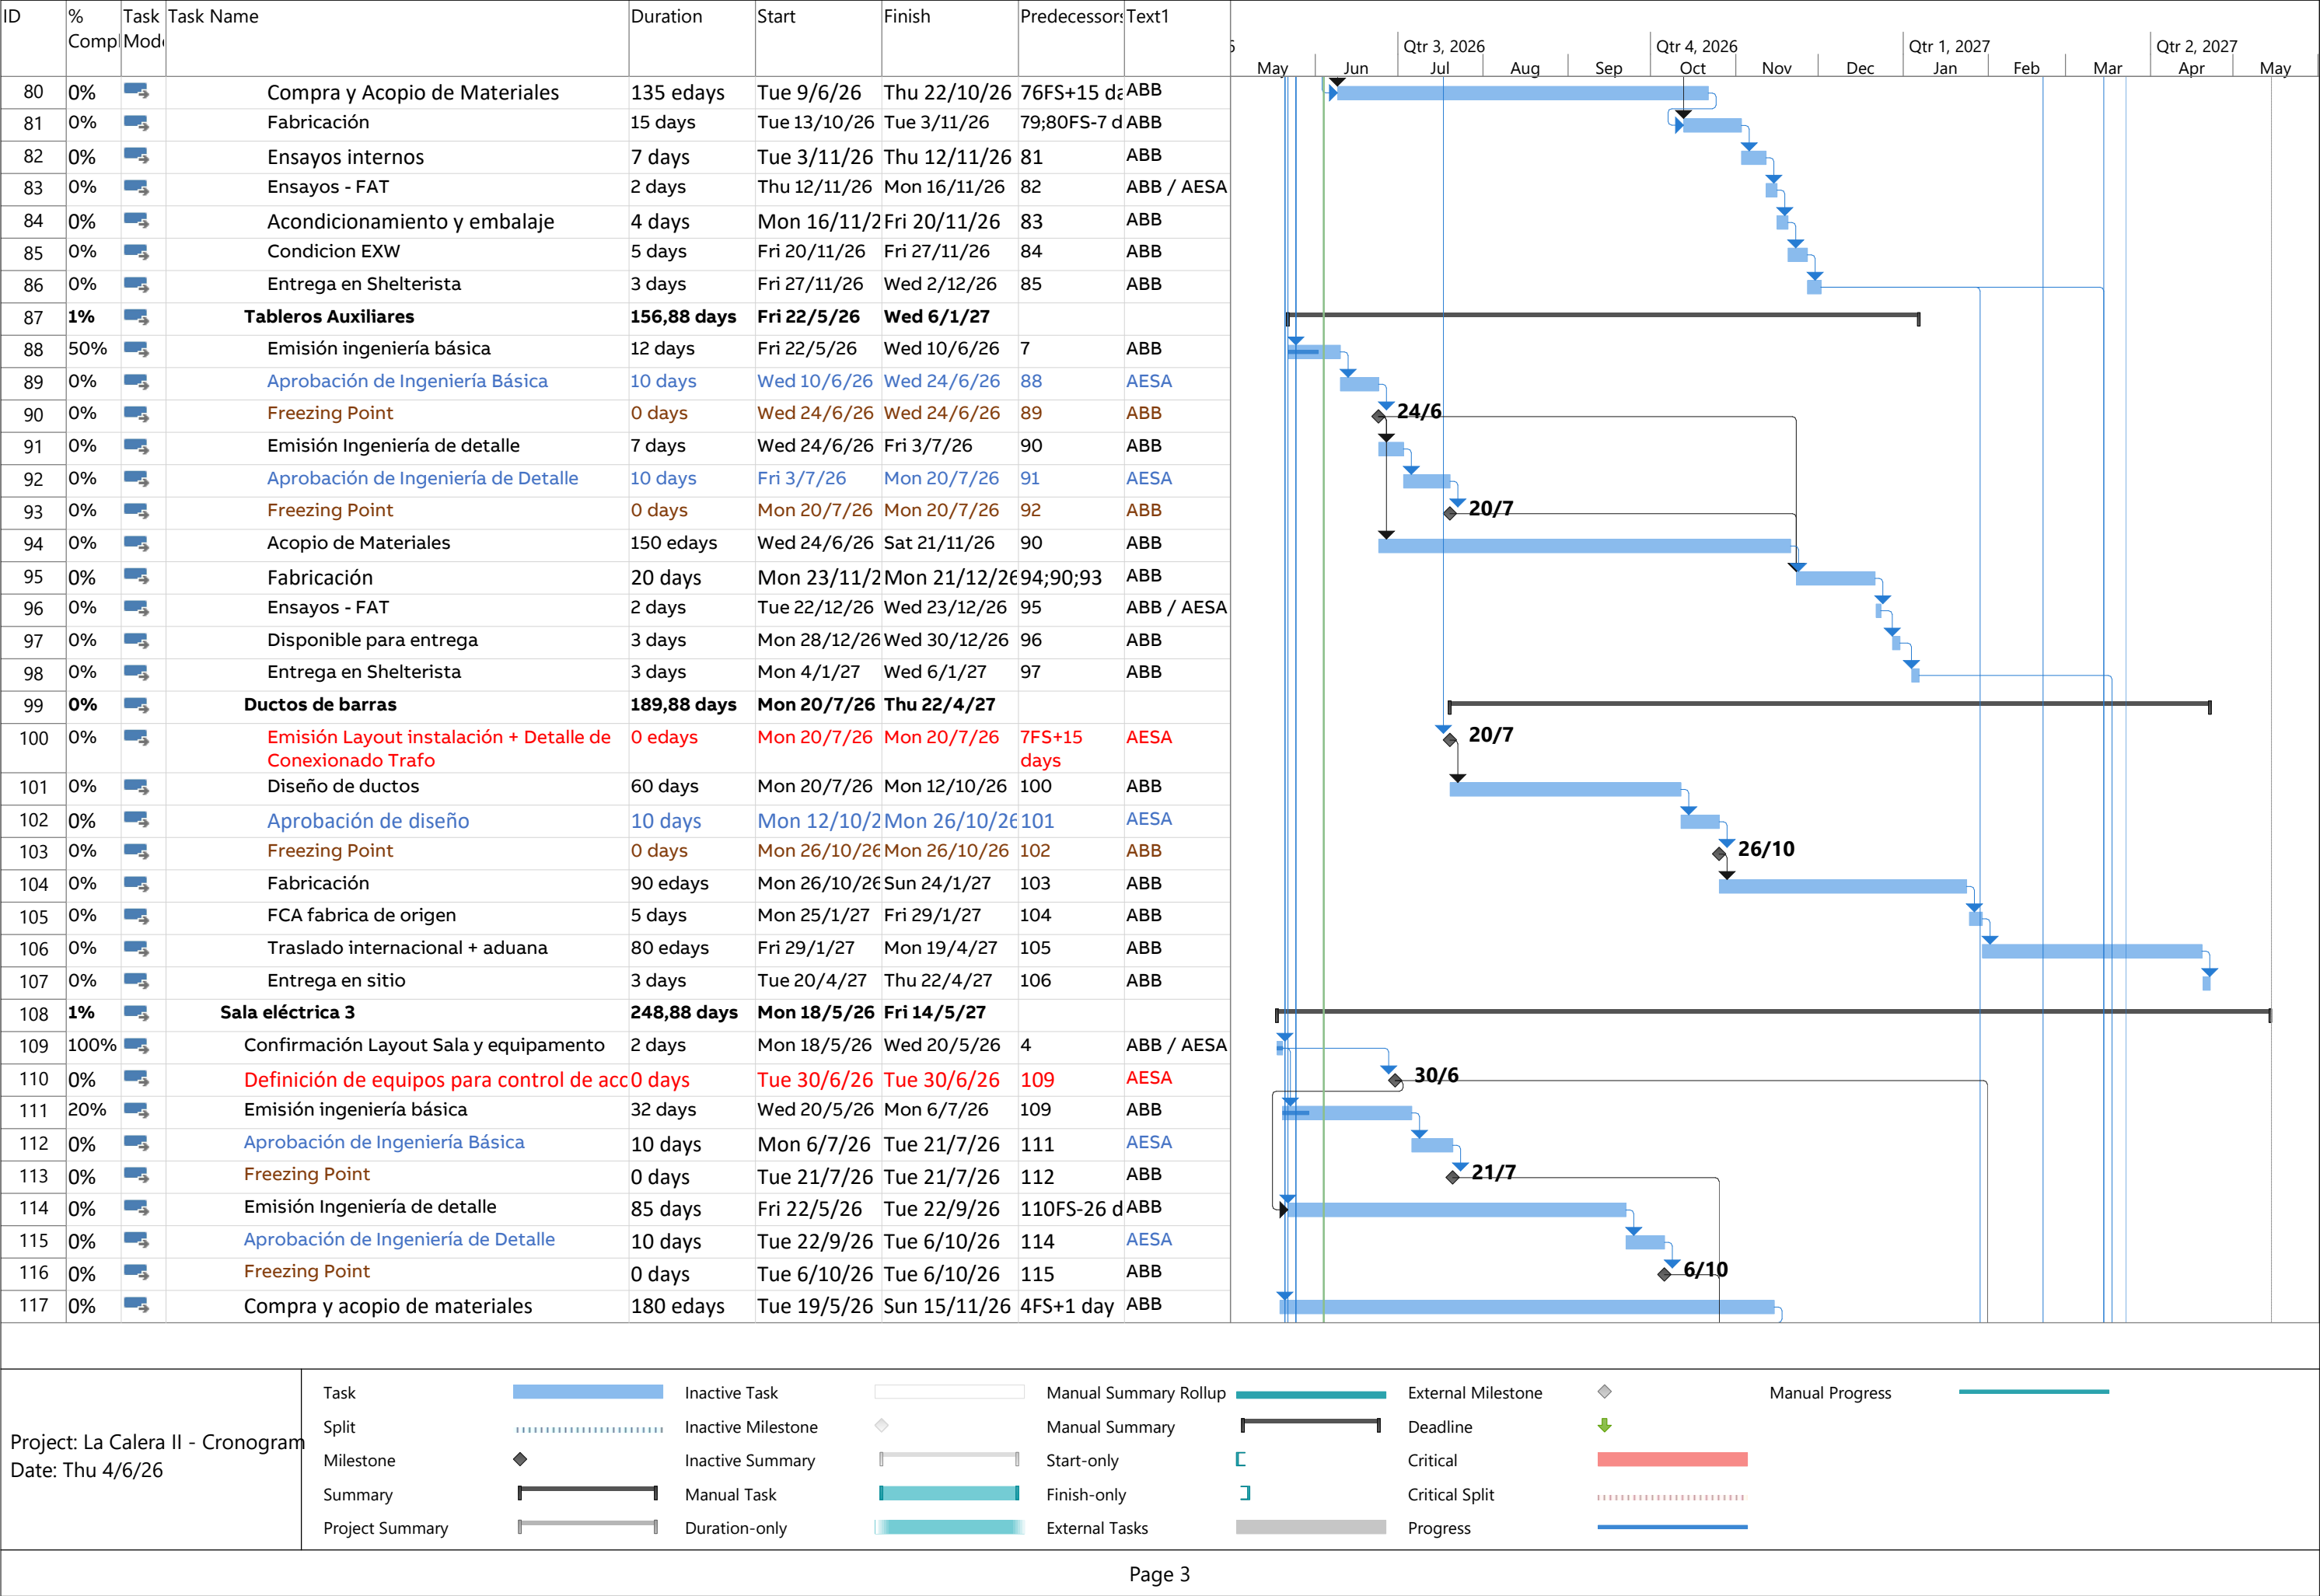

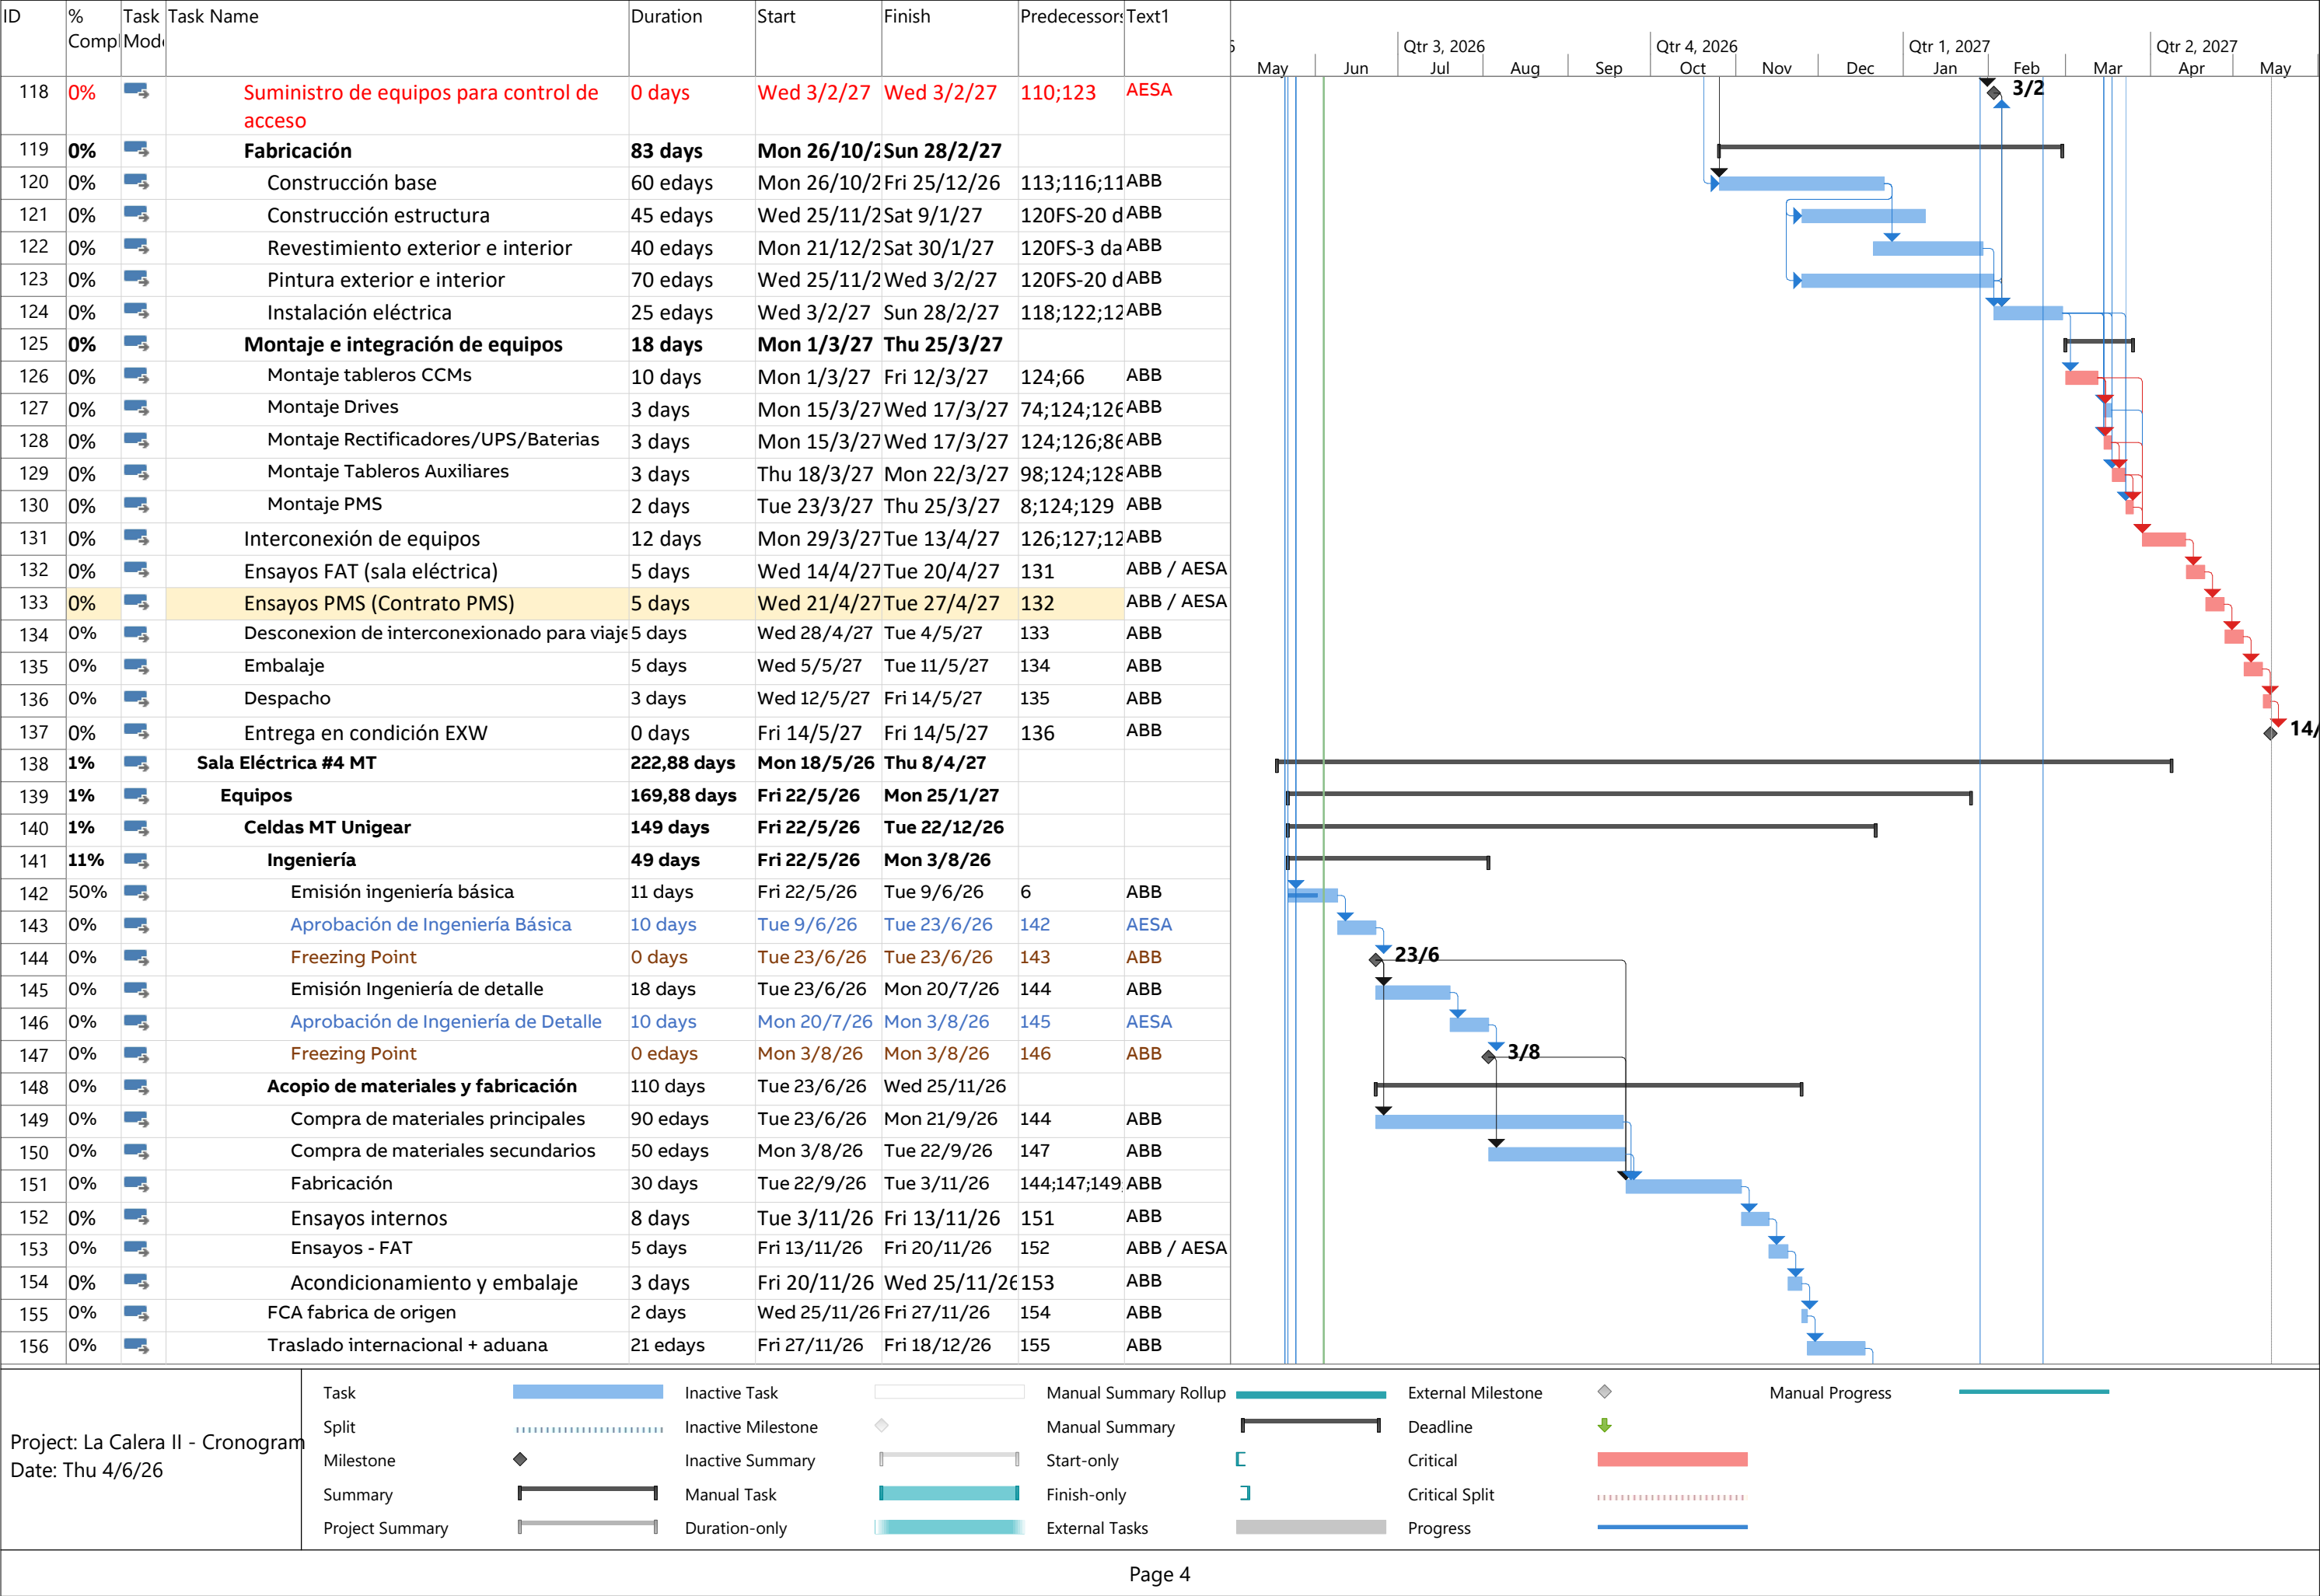

Page 4

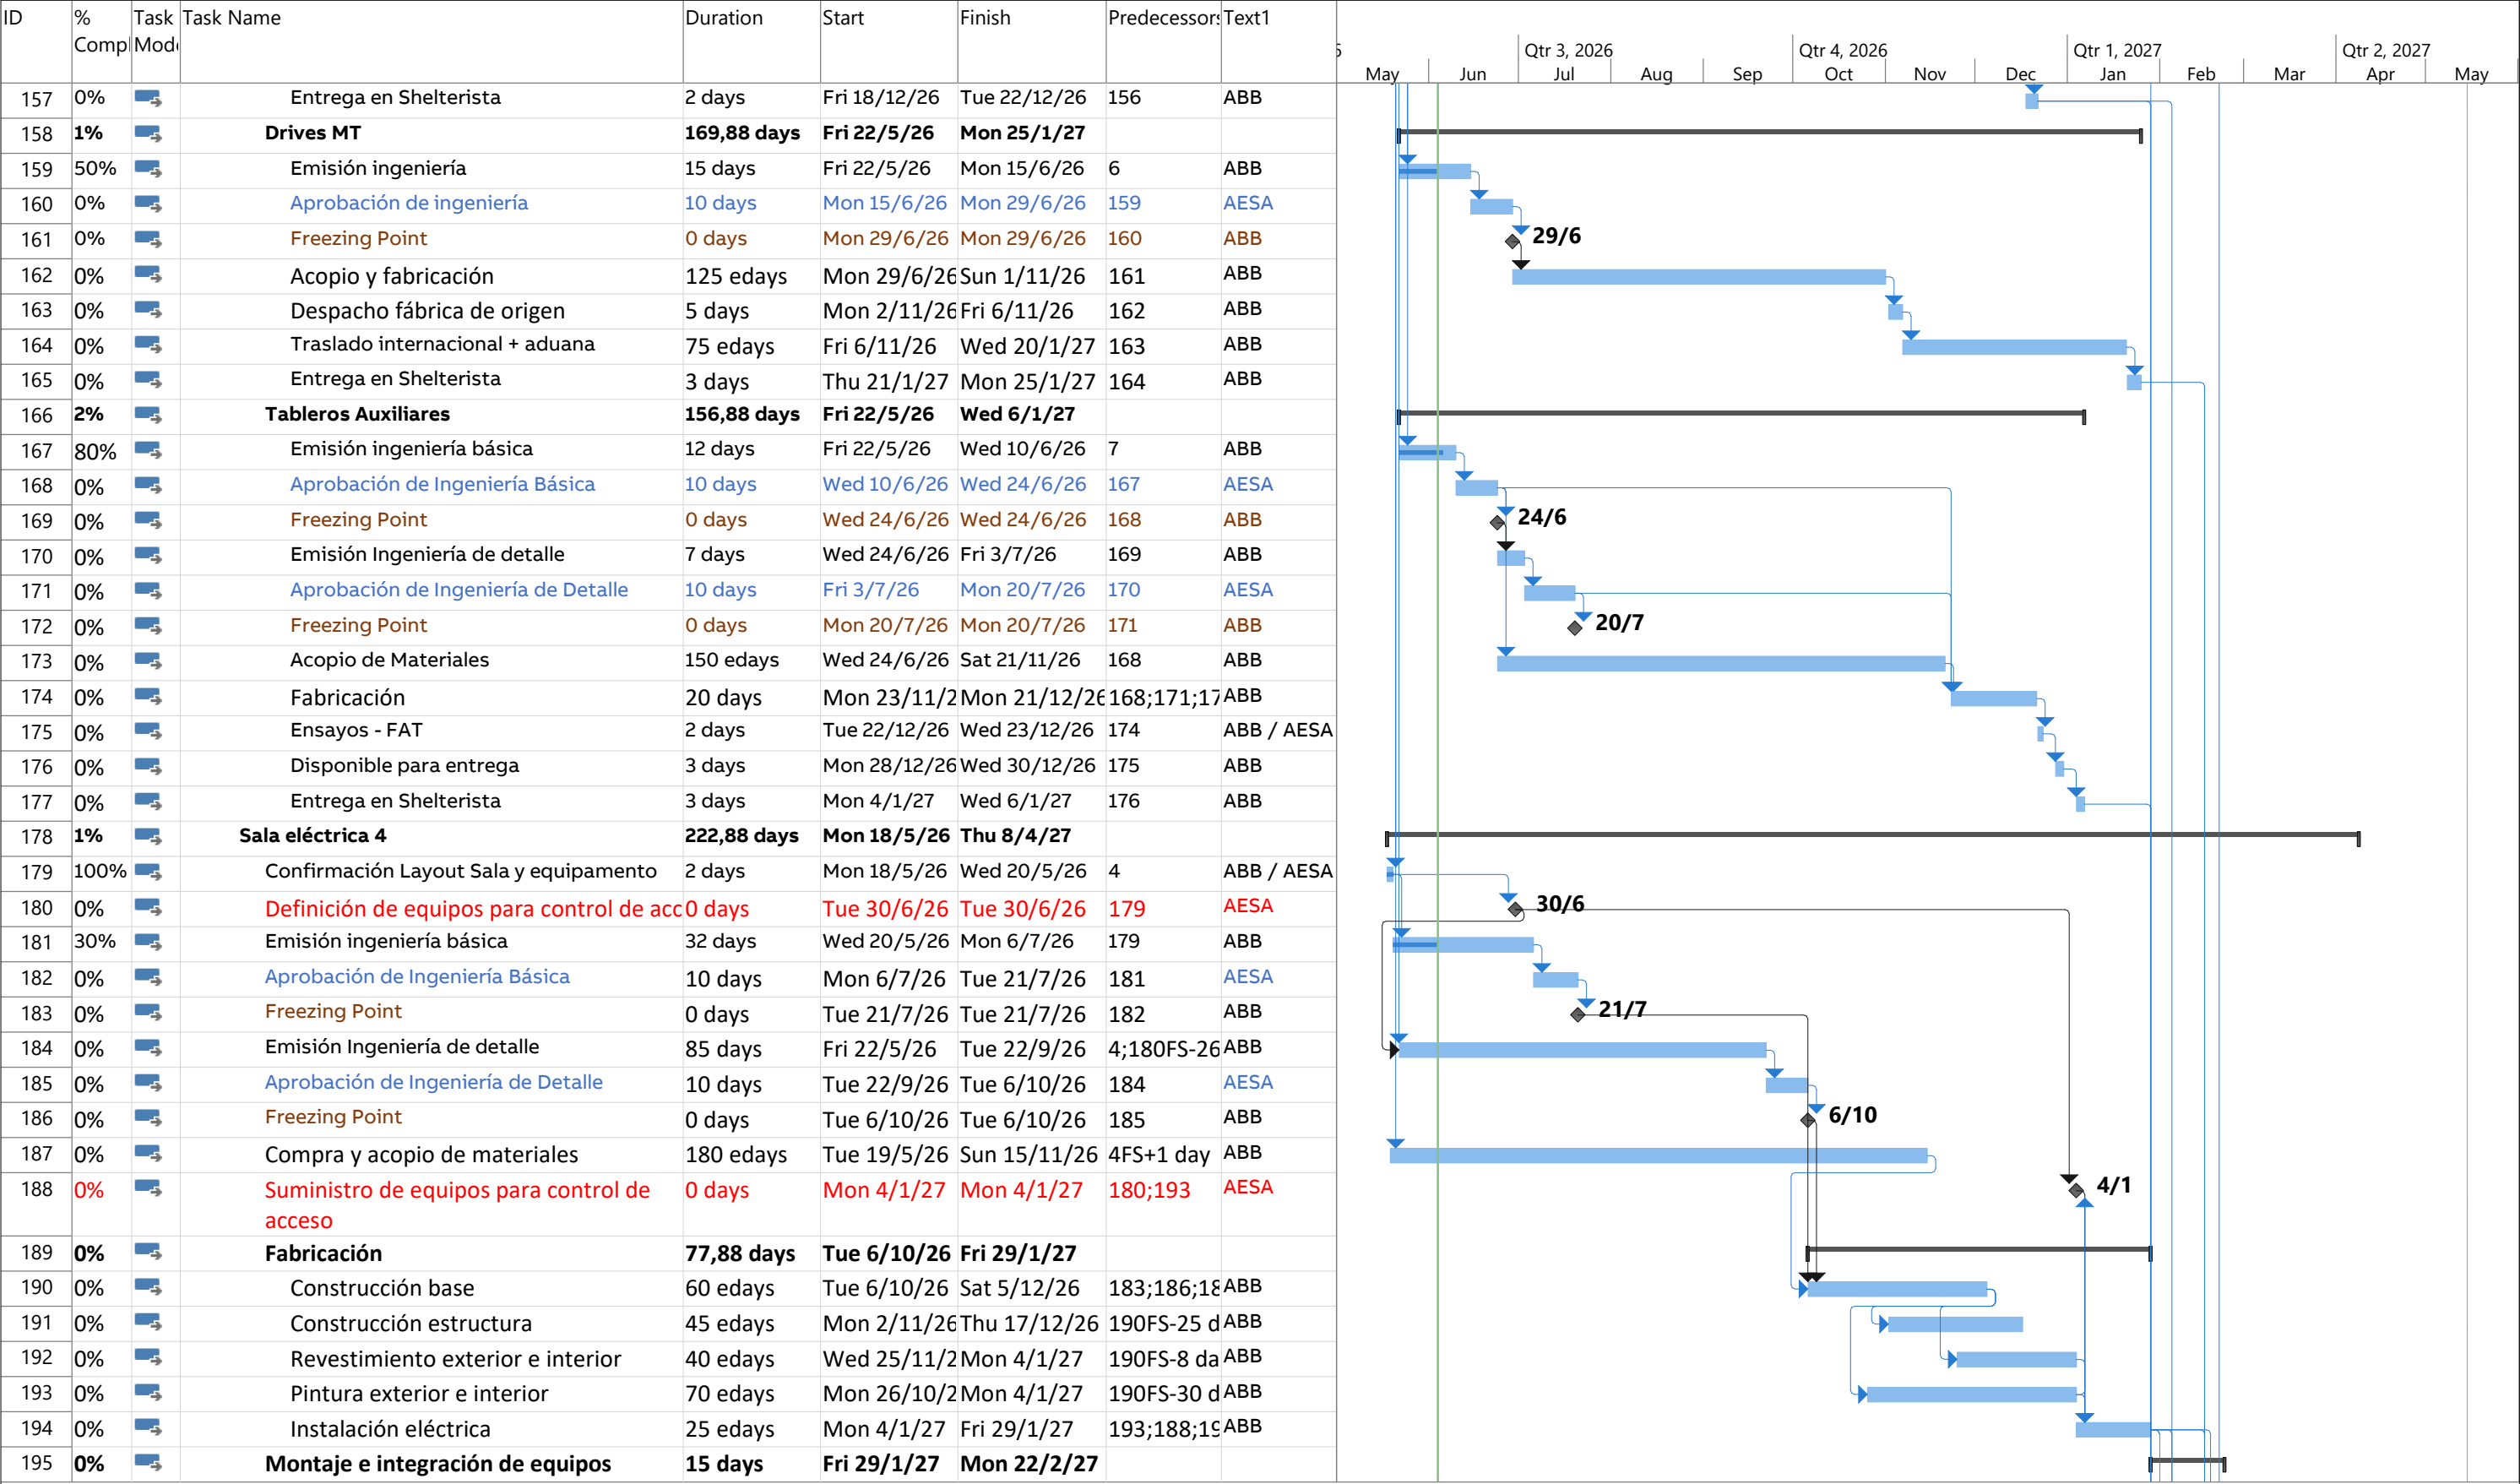

ID	% Comp	Task Mod	Task Name	Duration	Start	Finish	Predecessor	Text1	5 May Jun Qtr 3, 2026 Jul Aug Sep Qtr 4, 2026 Oct Nov Dec Qtr 1, 2027 Jan Feb Mar Qtr 2, 2027 Apr May																
196	0%		Montaje Tableros Auxiliares UPS	3 days	Fri 29/1/27	Tue 2/2/27	157;86;194	ABB																	
197	0%		Montaje Tableros Auxiliares	5 days	Fri 29/1/27	Thu 4/2/27	177;194	ABB																	
198	0%		Montaje Tablero MT	5 days	Fri 5/2/27	Mon 15/2/27	157;194;197	ABB																	
199	0%		Montaje Drives	5 days	Tue 16/2/27	Mon 22/2/27	165;194;198	ABB																	
200	0%		Montaje PMS	3 days	Thu 18/2/27	Mon 22/2/27	8;194	ABB																	
201	0%		Interconexión de equipos	10 days	Tue 23/2/27	Mon 8/3/27	196;197;199	ABB																	
202	0%		Ensayos FAT (sala eléctrica)	5 days	Tue 9/3/27	Mon 15/3/27	201	ABB / AESA																	
203	0%		Ensayos PMS (Contrato PMS)	5 days	Tue 16/3/27	Mon 22/3/27	202	ABB / AESA																	
204	0%		Desconexión de interconexión para viaje	5 days	Tue 23/3/27	Wed 31/3/27	203	ABB																	
205	0%		Embalaje	3 days	Thu 1/4/27	Mon 5/4/27	204	ABB																	
206	0%		Despacho	3 days	Tue 6/4/27	Thu 8/4/27	205	ABB																	
207	0%		Entrega en condición EXW	0 days	Thu 8/4/27	Thu 8/4/27	206	ABB																	

Project: La Calera II - Cronogram
Date: Thu 4/6/26

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
